



WEEKLY SUMMARY REPORT – CONTRACT WEEK 36

21-036 EAST NAPLES BAY

DREDGING AND ROCK REMOVAL PROJECT



Date: 5/27/2024 to 5/31/2024			
Inspectors: Mackenzie Hudson	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Days of Week: Monday to Friday	Contract Days: 246 to 250	Total Days: 250	Accident Report #: N/A
Canal(s) Worked In: A-A		Stations Worked Between: 13+20 to 13+60	

General

Remarks

#1 – Prime Contractor – Quality Enterprises:

Monday 5-27-2024:

- No on-site activity. Memorial Day.

Tuesday 5-28-2024:

- Turbidity curtain noted in place at station 6+00 in Canal A-A at 8:00am.
- Canal grinding in progress today in Canal A-A starting, approximately, at station 13+60.
- Contractor grinded rock from 8:00am to 12:00pm. Contractor left site and returned to resume grinding rock from 1:30pm to 4:45pm. Contractor dropped turbidity curtain, staged the equipment, and opened the canal at 5:00pm.
- Contractor has a barge, an excavator, one hopper, a fuel cube, a push boat staged overnight at station 13+50 in Canal A-A and a support boat at station 6+00 in Canal A-A while working on this canal. Contractor also has one hopper staged in Canal CC-CC between stations 1+00 and 2+00. In addition, the contractor has a long reach excavator, Epiroc grinder, Conex box, a fuel cube, and a water tank on trailer staged on the property located at 1300 Curlew Avenue, Naples, FL 34102. A GPS base station is also set up at this location during project work hours today.

Wednesday 5-29-2024:

- Turbidity curtain noted in place at station 6+00 in Canal A-A at 8:00am.
- Canal grinding in progress today in Canal A-A starting, approximately, at station 13+40.
- Contractor grinded rock from 8:00am to 5:00pm. Contractor dropped turbidity curtain, staged the equipment, and opened the canal at 5:05pm.
- Contractor has a barge, an excavator, one hopper, a fuel cube, a push boat staged overnight at station 13+50 in Canal A-A and a support boat at station 6+00 in Canal A-A while working on this canal. Contractor also has one hopper staged in Canal CC-CC between stations 1+00 and 2+00. In addition, the contractor has a long reach excavator, Epiroc grinder, Conex box, a fuel cube, and a water tank on trailer staged on the property located at 1300 Curlew Avenue, Naples, FL 34102. A GPS base station is also set up at this location during project work hours today.

Thursday 5-30-2024:

- Contractor waited for mechanic to arrive on site to weld and make repairs to the Epiroc grinder.



- Mechanic arrived on site at 2:15pm and worked on the Epiroc grinder until 4:45pm.
- Contractor has a barge, an excavator, one hopper, a fuel cube, a support boat, and a push boat staged overnight at station 4+00 in Canal Main B1 working on this canal. Contractor also has one hopper staged in Canal CC-CC between stations 1+00 and 2+00. In addition, the contractor has a long reach excavator, Epiroc grinder, Conex box, a fuel cube, and a water tank on trailer staged on the property located at 1300 Curlew Avenue, Naples, FL 34102. A GPS base station is also set up at this location during project work hours today.

Friday 5-31-2024:

- Turbidity curtain noted in place at station 6+00 in Canal A-A at 8:00am.
- Canal grinding in progress today in Canal A-A starting, approximately, at station 13+20 and moving to 13+40 in the northeast direction.
- Contractor grinded rock from 8:00am to 12:30pm. Contractor left site and returned to resume grinding rock from 2:00pm to 4:15pm. Contractor dropped turbidity curtain and staged the equipment at 4:30pm.
- Contractor has a barge, an excavator, one hopper, a fuel cube, a support boat, and a push boat staged overnight at station 4+00 in Canal Main B1 while working on this canal. Contractor also has one hopper staged in Canal CC-CC between stations 1+00 and 2+00. In addition, the contractor has a long reach excavator, Epiroc grinder, Conex box, a fuel cube, and a water tank on trailer staged on the property located at 1300 Curlew Avenue, Naples, FL 34102. A GPS base station is also set up at this location during project work hours today.

Note: Daily reports for the week attached.



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 5/27/2024			
Inspector: Mackenzie Hudson	Stantec PIN: 2028113191	Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Day of Week: Monday	Contract Day: 246	Week: 36	Accident Report #: N/A
High Temp (°F): 91 °F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 3:07 AM – 3.0'
Low Temp (°F): 72 °F	Wind: 5 to 7 mph	Wind: 9 to 10 mph	Low Tide: 9:36 AM – 1.7'
Canal Worked In: N/A	Stations Worked Between:	N/A	

General	
#1 – Prime Contractor – Quality Enterprises:	
<ul style="list-style-type: none"> No on-site activity. Memorial Day. 	

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Field Supervisor	0	0	Foreman	0	0
		Skilled Laborer	0	0	Unskilled Laborer	0	0	Safety Director	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	0	0
1	CAT 323	Excavator - Barge	1	0	0
1	CAT 326	Excavator – Long Reach	1	0	0
1	FL6223TB	Push Boat	1	0	0
1	FL2474PP	Support Boat	1	0	0
1	N/A	Hopper	2	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Mackenzie Hudson, EIT – CEI	From: N/A	To: N/A	0.0 hours



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 5/28/2024			
Inspector: Mackenzie Hudson	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Day of Week: Tuesday	Contract Day: 247	Week: 36	Accident Report #: N/A
High Temp (°F): 91 °F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 4:09 PM – 2.8'
Low Temp (°F): 77 °F	Wind: 4 to 9 mph	Wind: 12 to 15 mph	Low Tide: 10:32 AM – 1.7'
Canal Worked In: A-A	Stations Worked Between:	13+60	

General

#1 – Prime Contractor – Quality Enterprises:

- Turbidity curtain noted in place at station 6+00 in Canal A-A at 8:00am.
- Canal grinding in progress today in Canal A-A starting, approximately, at station 13+60.
- Contractor grinded rock from 8:00am to 12:00pm. Contractor left site and returned to resume grinding rock from 1:30pm to 4:45pm. Contractor dropped turbidity curtain, staged the equipment, and opened the canal at 5:00pm.
- Contractor has a barge, an excavator, one hopper, a fuel cube, a push boat staged overnight at station 13+50 in Canal A-A and a support boat at station 6+00 in Canal A-A while working on this canal. Contractor also has one hopper staged in Canal CC-CC between stations 1+00 and 2+00. In addition, the contractor has a long reach excavator, Epiroc grinder, Conex box, a fuel cube, and a water tank on trailer staged on the property located at 1300 Curlew Avenue, Naples, FL 34102. A GPS base station is also set up at this location during project work hours today.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Field Supervisor	0	0	Foreman	0	0
		Skilled Laborer	1	10	Unskilled Laborer	1	10	Safety Director	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	8
1	CAT 323	Excavator - Barge	1	1	8
1	CAT 326	Excavator – Long Reach	1	0	0
1	FL6223TB	Push Boat	1	1	8
1	FL2474PP	Support Boat	1	1	3
1	N/A	Hopper	2	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Mackenzie Hudson, EIT – CEI	From: 8:00 AM	To: 5:00 PM	8.0 hours



☀ 314°NW (T) ● 26°7'24"N, 81°47'2"W ±9ft ▲ 9ft



28 May 2024, 08:10:11

323 excavator grinding rock at station 13+60 in Canal A-A.



☀ 315°NW (T) ● 26°7'19"N, 81°47'6"W ±13ft ▲ 13ft



Turbidity curtain in place at station 6+00 in Canal A-A.

W 270 NW 330 N 0
40 270 300 330 0

☀ 310°NW (T) ☉ 26°7'24"N, 81°47'2"W ±9ft ▲ 28ft



28 May 2024, 09:31:02

323 excavator grinding rock at station 13+60 in Canal A-A.




☉ 312°NW (T) ☉ 26°7'24"N, 81°47'2"W ±16ft ▲ 7ft




323 excavator grinding rock at station 13+60 in Canal A-A.



☀ 338°N (T) ● 26°7'24"N, 81°47'2"W ±9ft ▲ 7ft

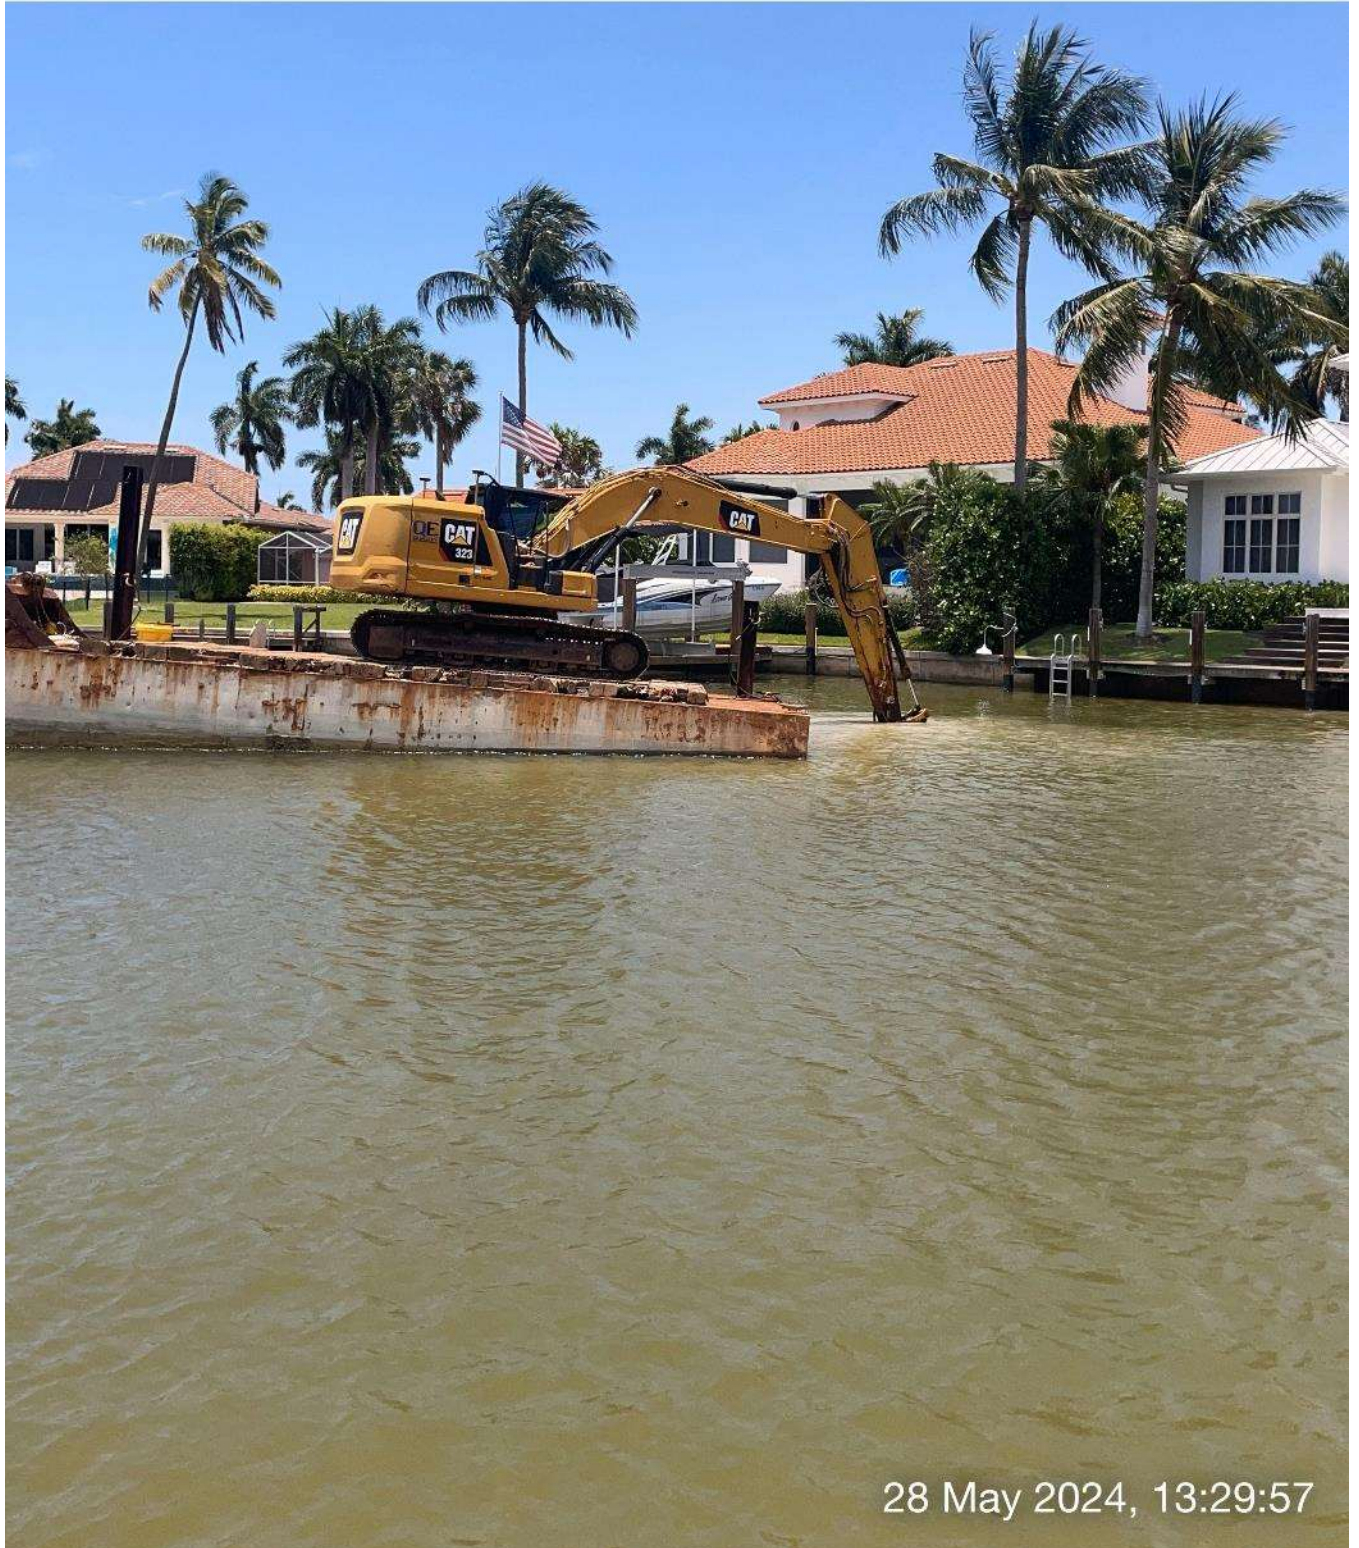

323 excavator grinding rock at station 13+60 in Canal A-A.



☀ 340°N (T) ● 26°7'24"N, 81°47'2"W ±13ft ▲ 16ft



28 May 2024, 15:04:30

323 excavator grinding rock at station 13+60 in Canal A-A.



☀ 353°N (T) ● 26°7'24"N, 81°47'2"W ±9ft ▲ 8ft



323 excavator grinding rock at station 13+60 in Canal A-A.



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 5/29/2024			
Inspector: Mackenzie Hudson	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Day of Week: Wednesday	Contract Day: 248	Week: 36	Accident Report #: N/A
High Temp (°F): 92 °F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 7:04 AM – 2.1'
Low Temp (°F): 75 °F	Wind: 5 to 8 mph	Wind: 12 to 14 mph	Low Tide: 12:23 PM – 1.6'
Canal Worked In: A-A	Stations Worked Between:	13+40	

General

#1 – Prime Contractor – Quality Enterprises:


- Turbidity curtain noted in place at station 6+00 in Canal A-A at 8:00am.
- Canal grinding in progress today in Canal A-A starting, approximately, at station 13+40.
- Contractor grinded rock from 8:00am to 5:00pm. Contractor dropped turbidity curtain, staged the equipment, and opened the canal at 5:05pm.
- Contractor has a barge, an excavator, one hopper, a fuel cube, a push boat staged overnight at station 13+50 in Canal A-A and a support boat at station 6+00 in Canal A-A while working on this canal. Contractor also has one hopper staged in Canal CC-CC between stations 1+00 and 2+00. In addition, the contractor has a long reach excavator, Epiroc grinder, Conex box, a fuel cube, and a water tank on trailer staged on the property located at 1300 Curlew Avenue, Naples, FL 34102. A GPS base station is also set up at this location during project work hours today.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Field Supervisor	0	0	Foreman	0	0
		Skilled Laborer	2	10	Unskilled Laborer	1	10	Safety Director	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	9
1	CAT 323	Excavator - Barge	1	1	9
1	CAT 326	Excavator – Long Reach	1	0	0
1	FL6223TB	Push Boat	1	1	9
1	FL2474PP	Support Boat	1	1	3
1	N/A	Hopper	2	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Mackenzie Hudson, EIT – CEI	From: 8:00 AM	To: 5:00 PM	8.0 hours



☀ 302°NW (T) ● 26°7'24"N, 81°47'2"W ±29ft ▲ 9ft



323 excavator grinding rock at station 13+40 in Canal A-A.




☀ 276°W (T) ● 26°7'19"N, 81°47'6"W ±9ft ▲ 25ft



29 May 2024, 08:08:50

Turbidity curtain in place at station 6+00 in Canal A-A.




☀ 307°NW (T) ● 26°7'24"N, 81°47'2"W ±9ft ▲ 9ft



29 May 2024, 09:41:30

323 excavator grinding rock at station 13+40 in Canal A-A.



☀ 306°NW (T) ● 26°7'24"N, 81°47'2"W ±9ft ▲ 11ft



29 May 2024, 11:01:11

323 excavator grinding rock at station 13+40 in Canal A-A.

W 270 NW 300 330 N 0 NE 30
☀ 336°NW (T) ☉ 26°7'24"N, 81°47'3"W ±13ft ▲ 11ft



29 May 2024, 13:02:47

323 excavator grinding rock at station 13+40 in Canal A-A.



☀ 335°NW (T) ☉ 26°7'24"N, 81°47'2"W ±13ft ▲ 20ft



29 May 2024, 14:41:28

323 excavator grinding rock at station 13+40 in Canal A-A.



☉ 333°NW (T) ☉ 26°7'24"N, 81°47'2"W ±9ft ▲ 11ft



29 May 2024, 16:33:14

323 excavator grinding rock at station 13+40 in Canal A-A.



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 5/30/2024			
Inspector: Mackenzie Hudson	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Day of Week: Thursday	Contract Day: 249	Week: 36	Accident Report #: N/A
High Temp (°F): 92 °F	AM Conditions: Sunny	PM Conditions: Sunny	High Tide: 7:44 AM – 2.3'
Low Temp (°F): 74 °F	Wind: 2 mph	Wind: 10 to 15 mph	Low Tide: 1:55 PM – 1.3'
Canal Worked In: N/A	Stations Worked Between:	N/A	

General

#1 – Prime Contractor – Quality Enterprises:

- Contractor waited for mechanic to arrive on site to weld and make repairs to the Epiroc grinder.
- Mechanic arrived on site at 2:15pm and worked on the Epiroc grinder until 4:45pm.
- Contractor has a barge, an excavator, one hopper, a fuel cube, a support boat, and a push boat staged overnight at station 4+00 in Canal Main B1 working on this canal. Contractor also has one hopper staged in Canal CC-CC between stations 1+00 and 2+00. In addition, the contractor has a long reach excavator, Epiroc grinder, Conex box, a fuel cube, and a water tank on trailer staged on the property located at 1300 Curlew Avenue, Naples, FL 34102. A GPS base station is also set up at this location during project work hours today.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Field Supervisor	0	0	Foreman	0	0
		Skilled Laborer	2	8	Unskilled Laborer	1	8	Safety Director	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	1
1	CAT 323	Excavator - Barge	1	1	1
1	CAT 326	Excavator – Long Reach	1	0	0
1	FL6223TB	Push Boat	1	1	1
1	FL2474PP	Support Boat	1	1	1
1	N/A	Hopper	2	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Mackenzie Hudson, EIT – CEI	From: 8:00 AM	To: 5:00 PM	8.0 hours

SW W NW
210 240 27 300 330

☀ 272°W (T) ☉ 26°7'24"N, 81°47'3"W ±13ft ▲ 21ft



30 May 2024, 09:00:52

Contractor exiting Canal A-A.


SE S SW
120 150 180 210 240
☀ 181°S (T) ☉ 26°7'24"N, 81°46'57"W ±16ft ▲ 20ft



Contractor waiting on mechanic to arrive on site.



☉ 170°S (T) ● 26°7'24"N, 81°46'57"W ±13ft ▲ 10ft

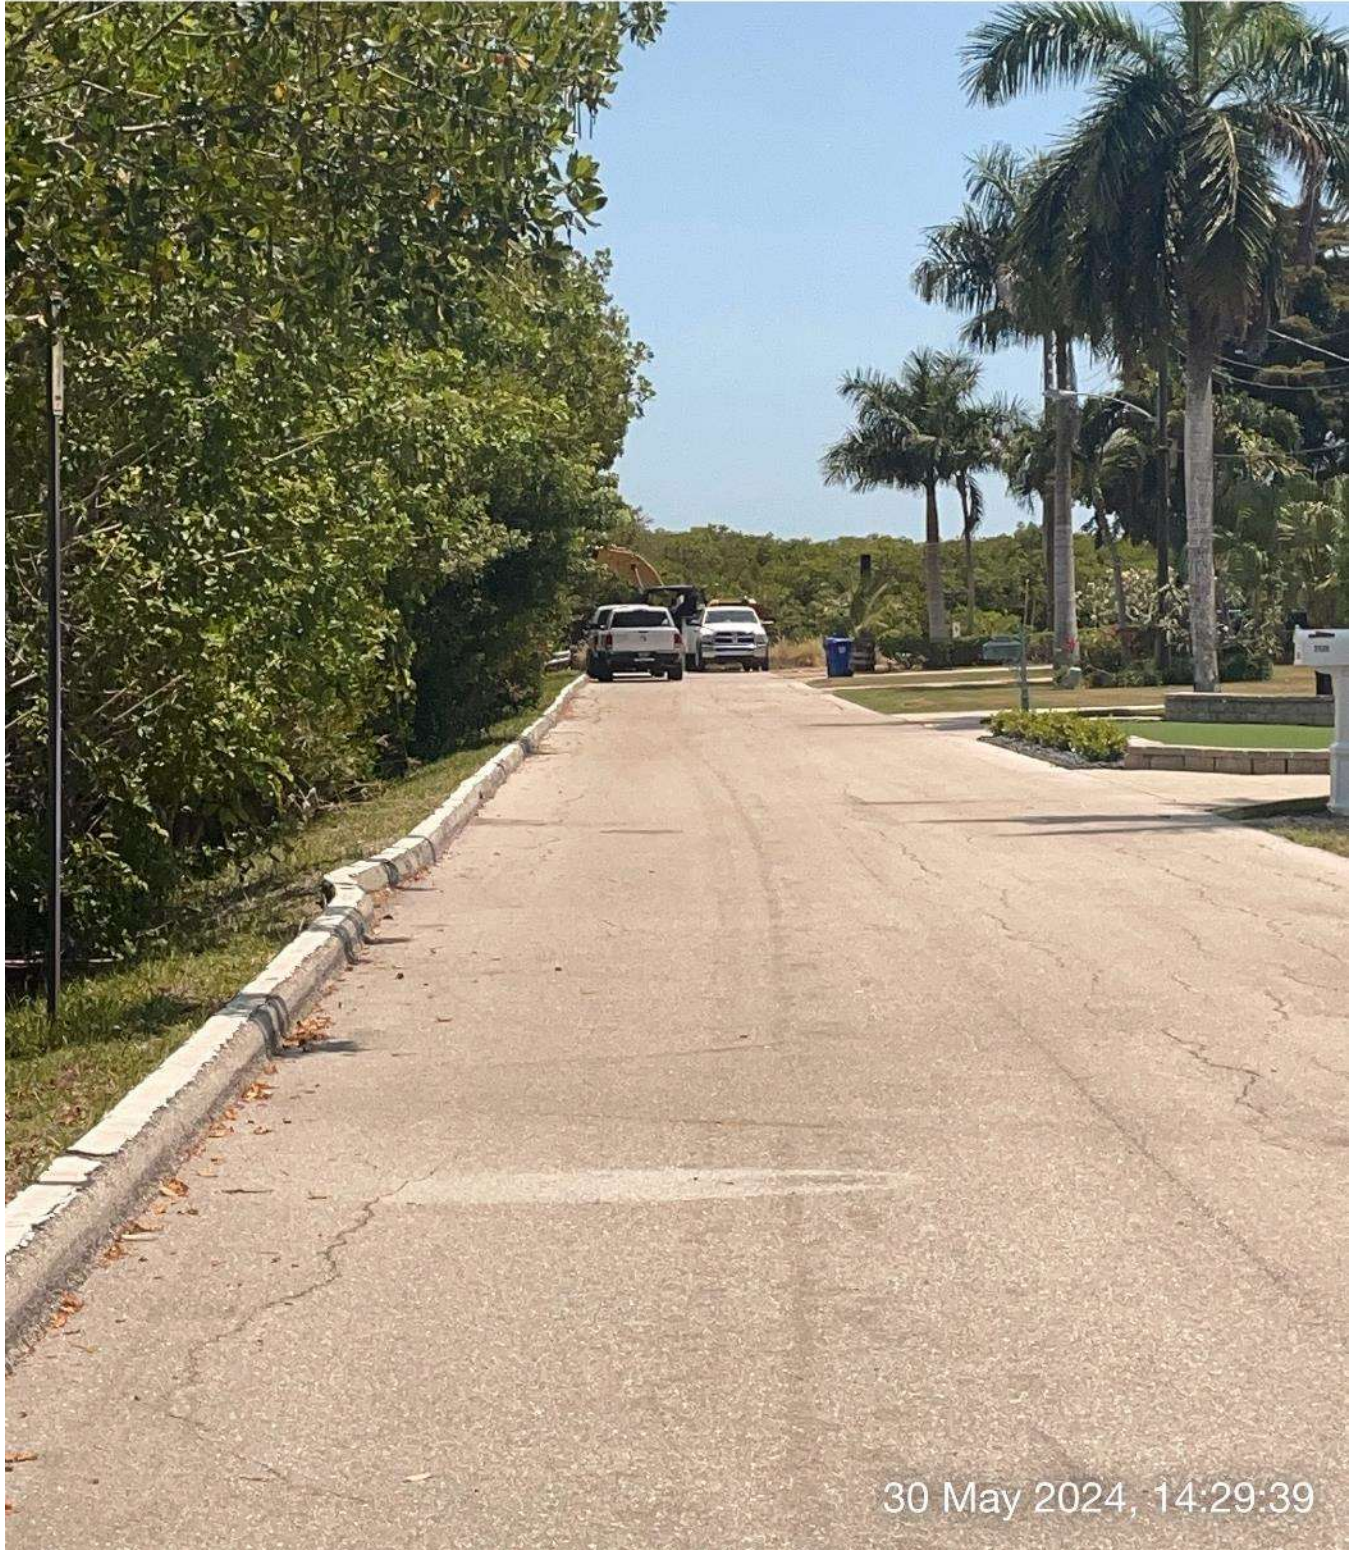

30 May 2024, 14:29:39

Mechanic arriving on site.



☀ 172°S (T) ● 26°7'24"N, 81°46'57"W ±13ft ▲ 9ft



Equipment staged at station 4+00 in Canal Main B1.



DAILY REPORT OF CONSTRUCTION
 21-036 EAST NAPLES BAY
 DREDGING AND ROCK REMOVAL PROJECT



Date: 5/31/2024			
Inspector: Mackenzie Hudson	Stantec PIN: 2028113191		Accidents <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Day of Week: Friday	Contract Day: 250	Week: 36	Accident Report #: N/A
High Temp (°F): 94 °F	AM Conditions: Cloudy	PM Conditions: Cloudy	High Tide: 8:25 AM – 2.5'
Low Temp (°F): 72 °F	Wind: 9 to 10 mph	Wind: 3 to 5 mph	Low Tide: 3:03 PM – 0.9'
Canal Worked In: A-A	Stations Worked Between:	13+20 to 13+40	

General

#1 – Prime Contractor – Quality Enterprises:

- Turbidity curtain noted in place at station 6+00 in Canal A-A at 8:00am.
- Canal grinding in progress today in Canal A-A starting, approximately, at station 13+20 and moving to 13+40 in the northeast direction.
- Contractor grinded rock from 8:00am to 12:30pm. Contractor left site and returned to resume grinding rock from 2:00pm to 4:15pm. Contractor dropped turbidity curtain and staged the equipment at 4:30pm.
- Contractor has a barge, an excavator, one hopper, a fuel cube, a support boat, and a push boat staged overnight at station 4+00 in Canal Main B1 while working on this canal. Contractor also has one hopper staged in Canal CC-CC between stations 1+00 and 2+00. In addition, the contractor has a long reach excavator, Epiroc grinder, Conex box, a fuel cube, and a water tank on trailer staged on the property located at 1300 Curlew Avenue, Naples, FL 34102. A GPS base station is also set up at this location during project work hours today.

Contractor(s) and Personnel										
#	Name	Type	#	Hrs.	Type	#	Hrs.	Type	#	Hrs.
1	Prime: Quality Enterprises	PM	0	0	Field Supervisor	0	0	Foreman	0	0
		Skilled Laborer	2	10	Unskilled Laborer	1	10	Safety Director	0	0

Equipment					
Cont/ Sub #	Equipment ID	Description	# Pieces	# Used	Total Hours Used
1	N/A	Barge	1	1	7
1	CAT 323	Excavator - Barge	1	1	7
1	CAT 326	Excavator – Long Reach	1	0	0
1	FL6223TB	Push Boat	1	1	7
1	FL2474PP	Support Boat	1	1	3
1	N/A	Hopper	2	0	0

Visitors			
Name	Company	Hours at Job Site	
		From:	To:

Inspector Name and Position	Hours at Job Site/Office		Total Hours
Mackenzie Hudson, EIT – CEI	From: 8:00 AM	To: 5:00 PM	8.0 hours



☀ 330°NW (T) ● 26°7'24"N, 81°47'3"W ±9ft ▲ 11ft



31 May 2024, 07:59:48

323 excavator grinding rock at station 13+20 in Canal A-A.


SW W NW
210 240 270 300 330

☀ 265°W (T) ☉ 26°7'19"N, 81°47'6"W ±13ft ▲ 10ft



31 May 2024, 08:03:27

Turbidity curtain in place at station 6+00 in Canal A-A.




☀ 306°NW (T) ☉ 26°7'24"N, 81°47'2"W ±13ft ▲ 7ft



31 May 2024, 09:36:10

323 excavator grinding rock at station 13+40 in Canal A-A.



☀ 304°NW (T) ● 26°7'24"N, 81°47'2"W ±16ft ▲ 9ft



31 May 2024, 11:06:44

323 excavator grinding rock at station 13+40 in Canal A-A.

W 270 NW 300 330 N 0 N 30
☀ 335°NW (T) ☉ 26°7'24"N, 81°47'3"W ±13ft ▲ 9ft



31 May 2024, 14:08:11

323 excavator grinding rock at station 13+40 in Canal A-A.



☉ 329°NW (T) ☉ 26°7'24"N, 81°47'2"W ±9ft ▲ 15ft



323 excavator grinding rock at station 13+40 in Canal A-A.



☉ 179°S (T) ☉ 26°7'24"N, 81°46'56"W ±13ft ▲ 13ft



31 May 2024, 16:29:45

Equipment staged at station 4+00 in Canal Main B1.
